

Overview of work completed August 31 - September 11, 2026

Tested Recycle Line
Installed Recycle Meter
Installed Pipe Supports in Cell 2
Placed Concrete for Aerator Ballast, Mooring
Posts, Caissons, and Sidewalk Replacement
Set Recycle Pumps, Breakaways and Slide Rails
Replaced Gate Valve Between Cell 3 and Chlorine
Contact Chamber




Pressure Testing the Recycle Line



Auguring Holes for Mooring Posts & Caissons



Preparing to pour concrete ballast for SSI Aeration

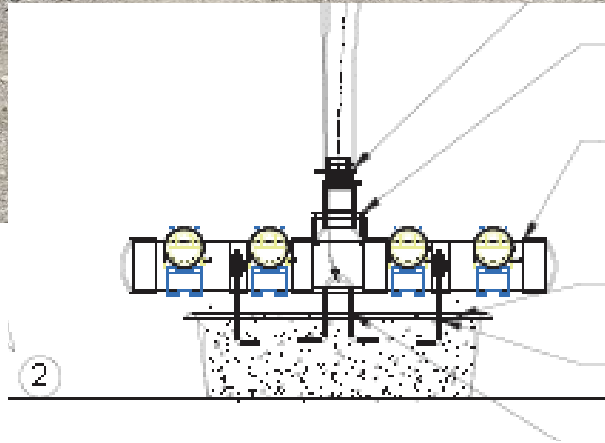

Placing Concrete



Placing Inlet Pipe Supports in Cell 2




Find the leak in
Cell 2 Inlet



Repairing the Leak



Leak Repair (continued)

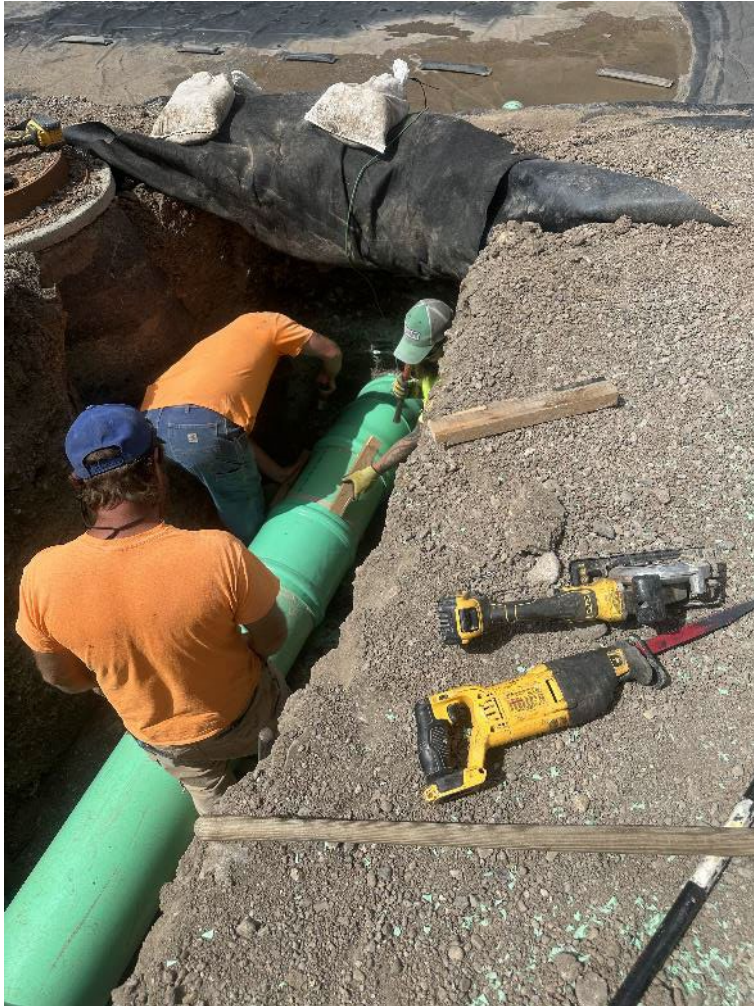

Replaced Gate Valve between Cell 3 and Chlorine Contact Chamber



Started Leak Test of Cell 2



Wiring Electrical Panels and Blowers



Work for the Week Ahead

- Leak Test Cell 2
- Site Piping for Modules
- Potentially start treating sewage in New Cell 2 & Renovating the Concrete Basin
- Continuing Wiring Electrical
