


Overview of work completed November 1-15, 2025

- Working the berms for new Cells 1 and 2
- Hauled some sludge to Whinnery's
- Began Treatment in the new polishing pond
- Began building the berm for new cells 1 and 2
- Removed most of the old aeration system
- Finished temporary air pipe and backfilled around the building
- Tiger worked rough in electrical
- Triple Z installed skylight and some soffit and fascia



Removal & Clean up Old Aeration System

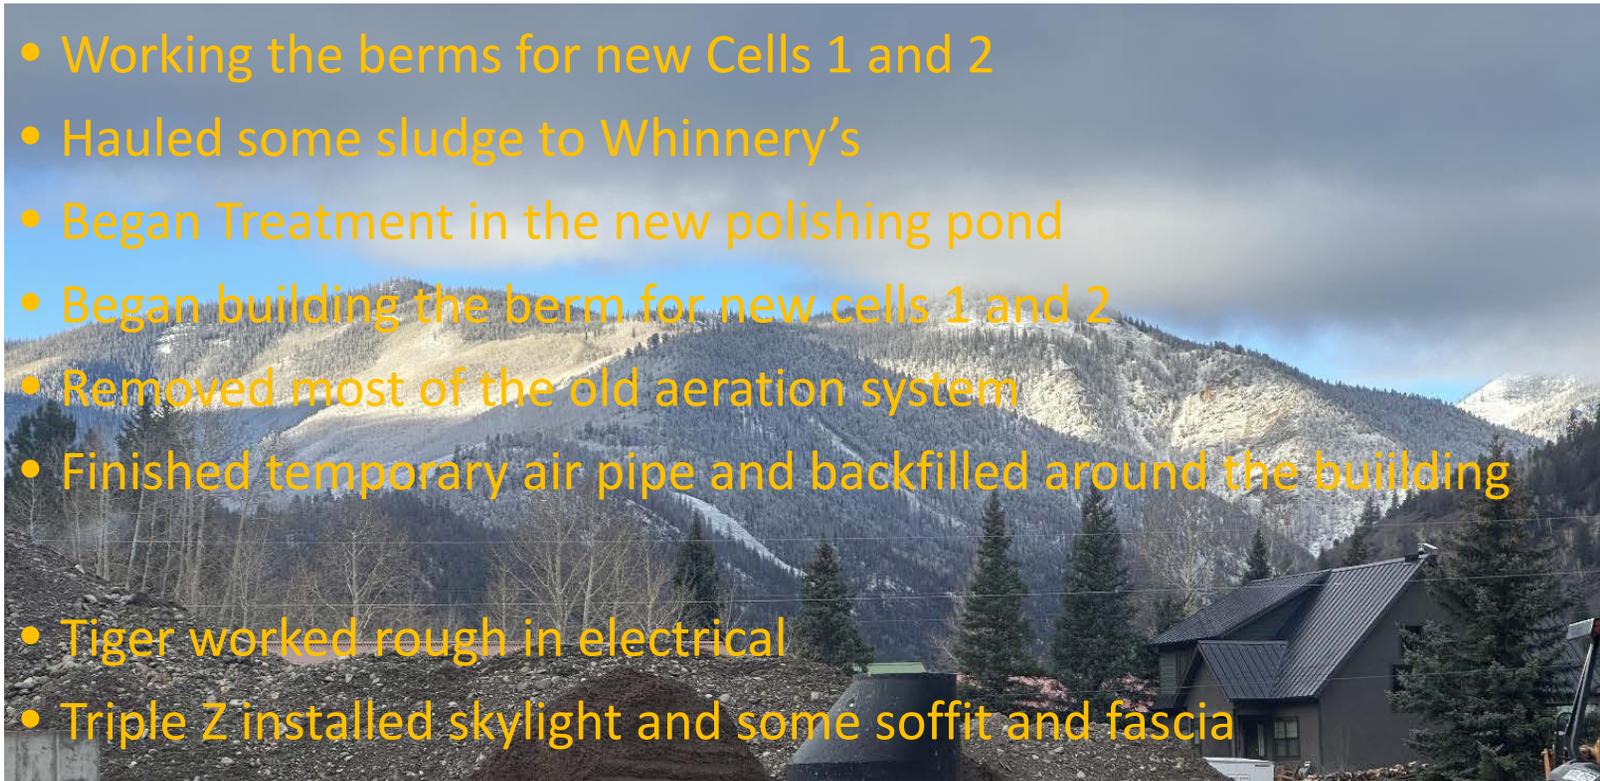

Sludge Removal



Transfer sludge to temporary area East of the new N/S berm



Berm Construction



Berm Construction



Berm Construction



Winter is coming




Initial Stockpile
Disappearing (they need
lots more dirt)



Air Pipe by Bldg



Skylight Install

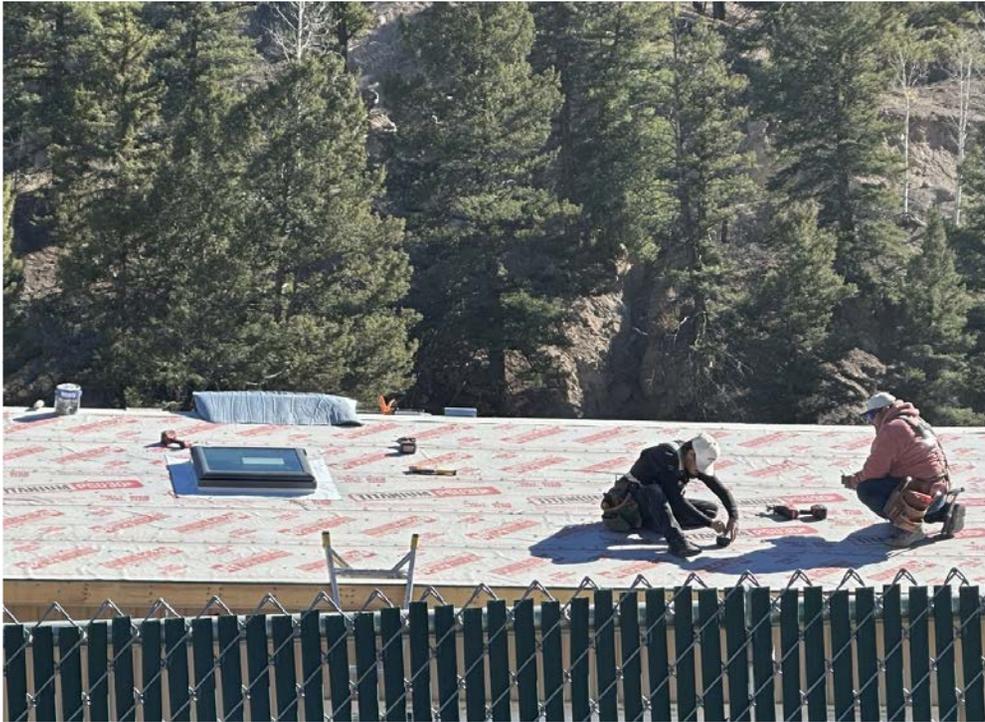

Building Sheathing & Trim



Electrical Rough in

