

Overview of work completed October 5-16, 2026

Finished cleaning out and lining the concrete basin

Unloaded, seamed together and placed insulated covers on the 3 ponds and concrete basin.

Installed anchors for covers

Installed aeration equipment in Cell 2 and the Concrete Basin

Installed ventilation and heaters in new building

Continued working on wiring in the new building & extending to the aeration basins

Completed blower startup, transferred aeration equipment to the new blowers and removed old blower

Placing Under Liner Vents in Concrete Basin



Lining the Concrete Basin



Removing insulated cover casings from the delivery truck



Seaming casings of the cover together



Placing cover on the lagoons



Installing the Baffle Curtain



Placing duckbill tie downs to secure cover



Placing Aerators



Placing Aerator/Mixer in Concrete Basin




Removing the
old blowers




Cleaning out things
that had been stashed
in the blower room.

Preparing to load to take to the
dump

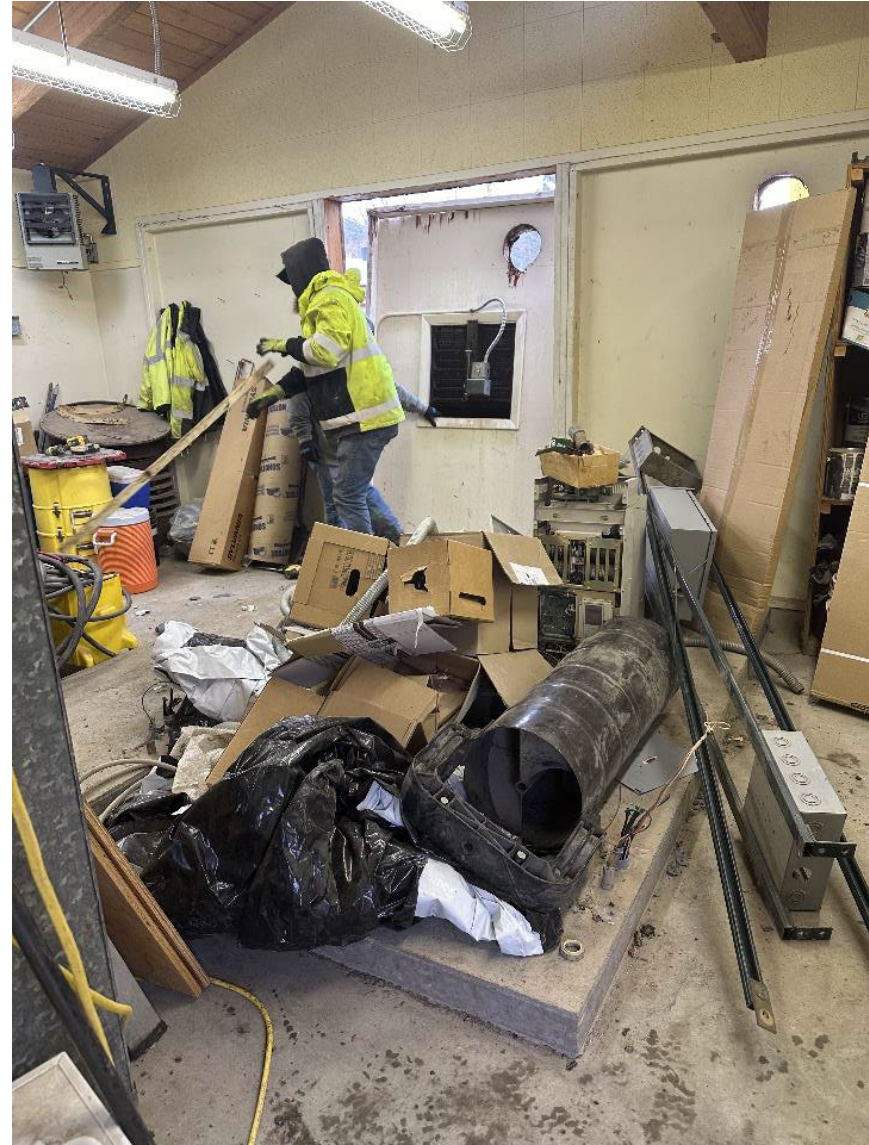

Ventilation Equipment Installed

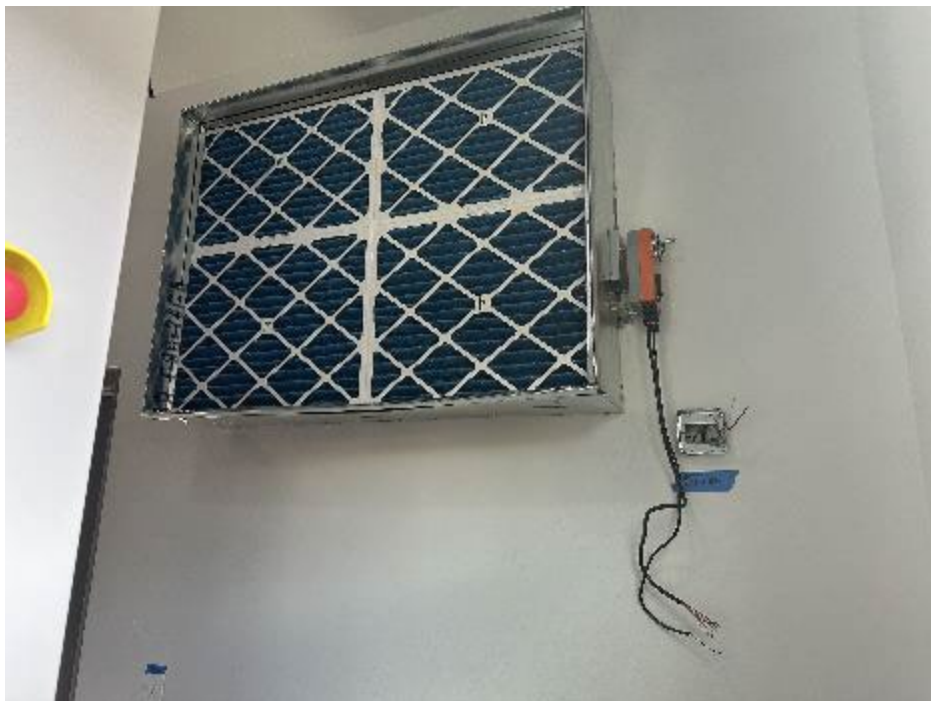

Heater Install



Work for the week ahead

- Install Aeration in Cell 1
- Remove existing switch gear (elec panel) and install new power panel in existing building & town shop
- Generator Fuel Tank Testing & Start up
- Continuing wiring electrical improvements
- Gutters, mopboard, interior door & odds and end in new building.
