

Overview of work completed September 14, - October 3, 2026

- Placed Liner Material under modules and aerator anchors
- Placed pipe supports under inlet pipes
- Received Slide gates and installed them
- Piped and placed modules in Cell 2, installed temp baffle
- Did some fence preparation
- Installed snow rails and worked on solar tubes
- Removed sludge from concrete basin
- Received temporary power for the new blower building


Installed liner under aeration equipment



Installed pipe supports under inlet pipes



Installed snow rails, worked on solar tubes

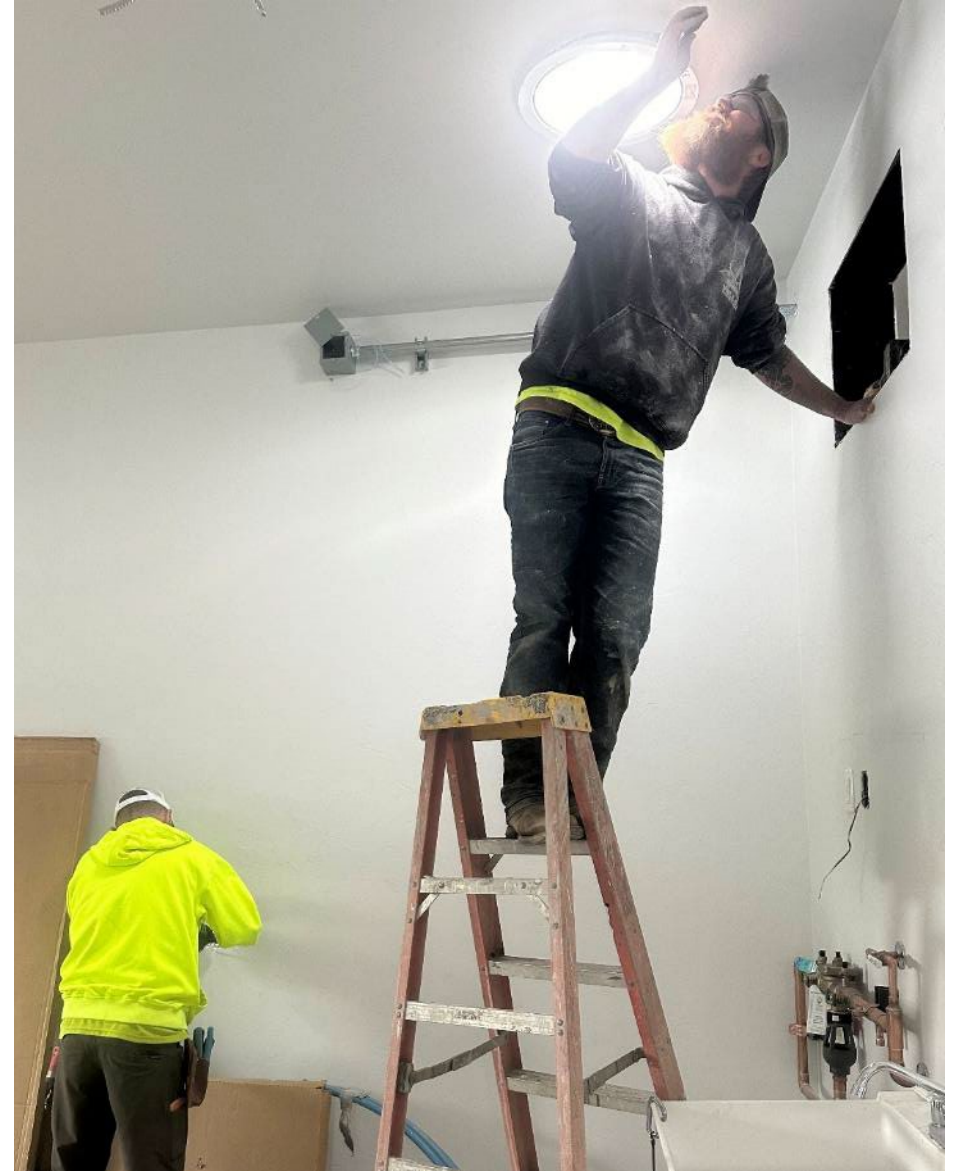

Slide gates arrive (after 12 week wait)



Start installing
slide gates



Slide gates not
sealing properly





Repairing Slide gates



Installing Slide Gate



Placing modules in Cell 2 (temporarily)



Will be removed for cover installation
and then set permanently thru the cover



Installing Lifting Cables on the Modules



Installing Temporary Baffle Curtain Cell 2



Dewatering the Concrete Basin



Town Crew Assembling Aspirators (Mixer and Aeration Equipment)



Concrete Basin Sludge Removal Before

and

Almost After



Wiring between Blowers and disconnects





Work for the Week Ahead

- Set covers
- Line Concrete Basin
- Blower Start up
- Continuing wiring electrical improvements

